DELIVERY PLAN · UPDATED 28 SEP 2026

Visita launch timeline

From today to a public launch in Cagayan de Oro on Tuesday 29 December: the core visitor and venue-owner flows first, then stakeholder testing, fixes, an open beta, and a final round of fixes.

> **Still to come from the client side:** the final UI/UX and branding, and the business model. Until they arrive, screens use the PRD's provisional colours and type, and pricing uses placeholder founder rates. The dates each one is needed by are in the chart and under "Waiting on the client or project head".

Tue 29 Dec 2026	13 weeks	2 checkpoints	6 check-ins	4 inputs needed
Launch	28 Sep – 28 Dec	23 Oct · 6 Nov	Bi-weekly, with the project head	First one by Fri 9 Oct

Schedule

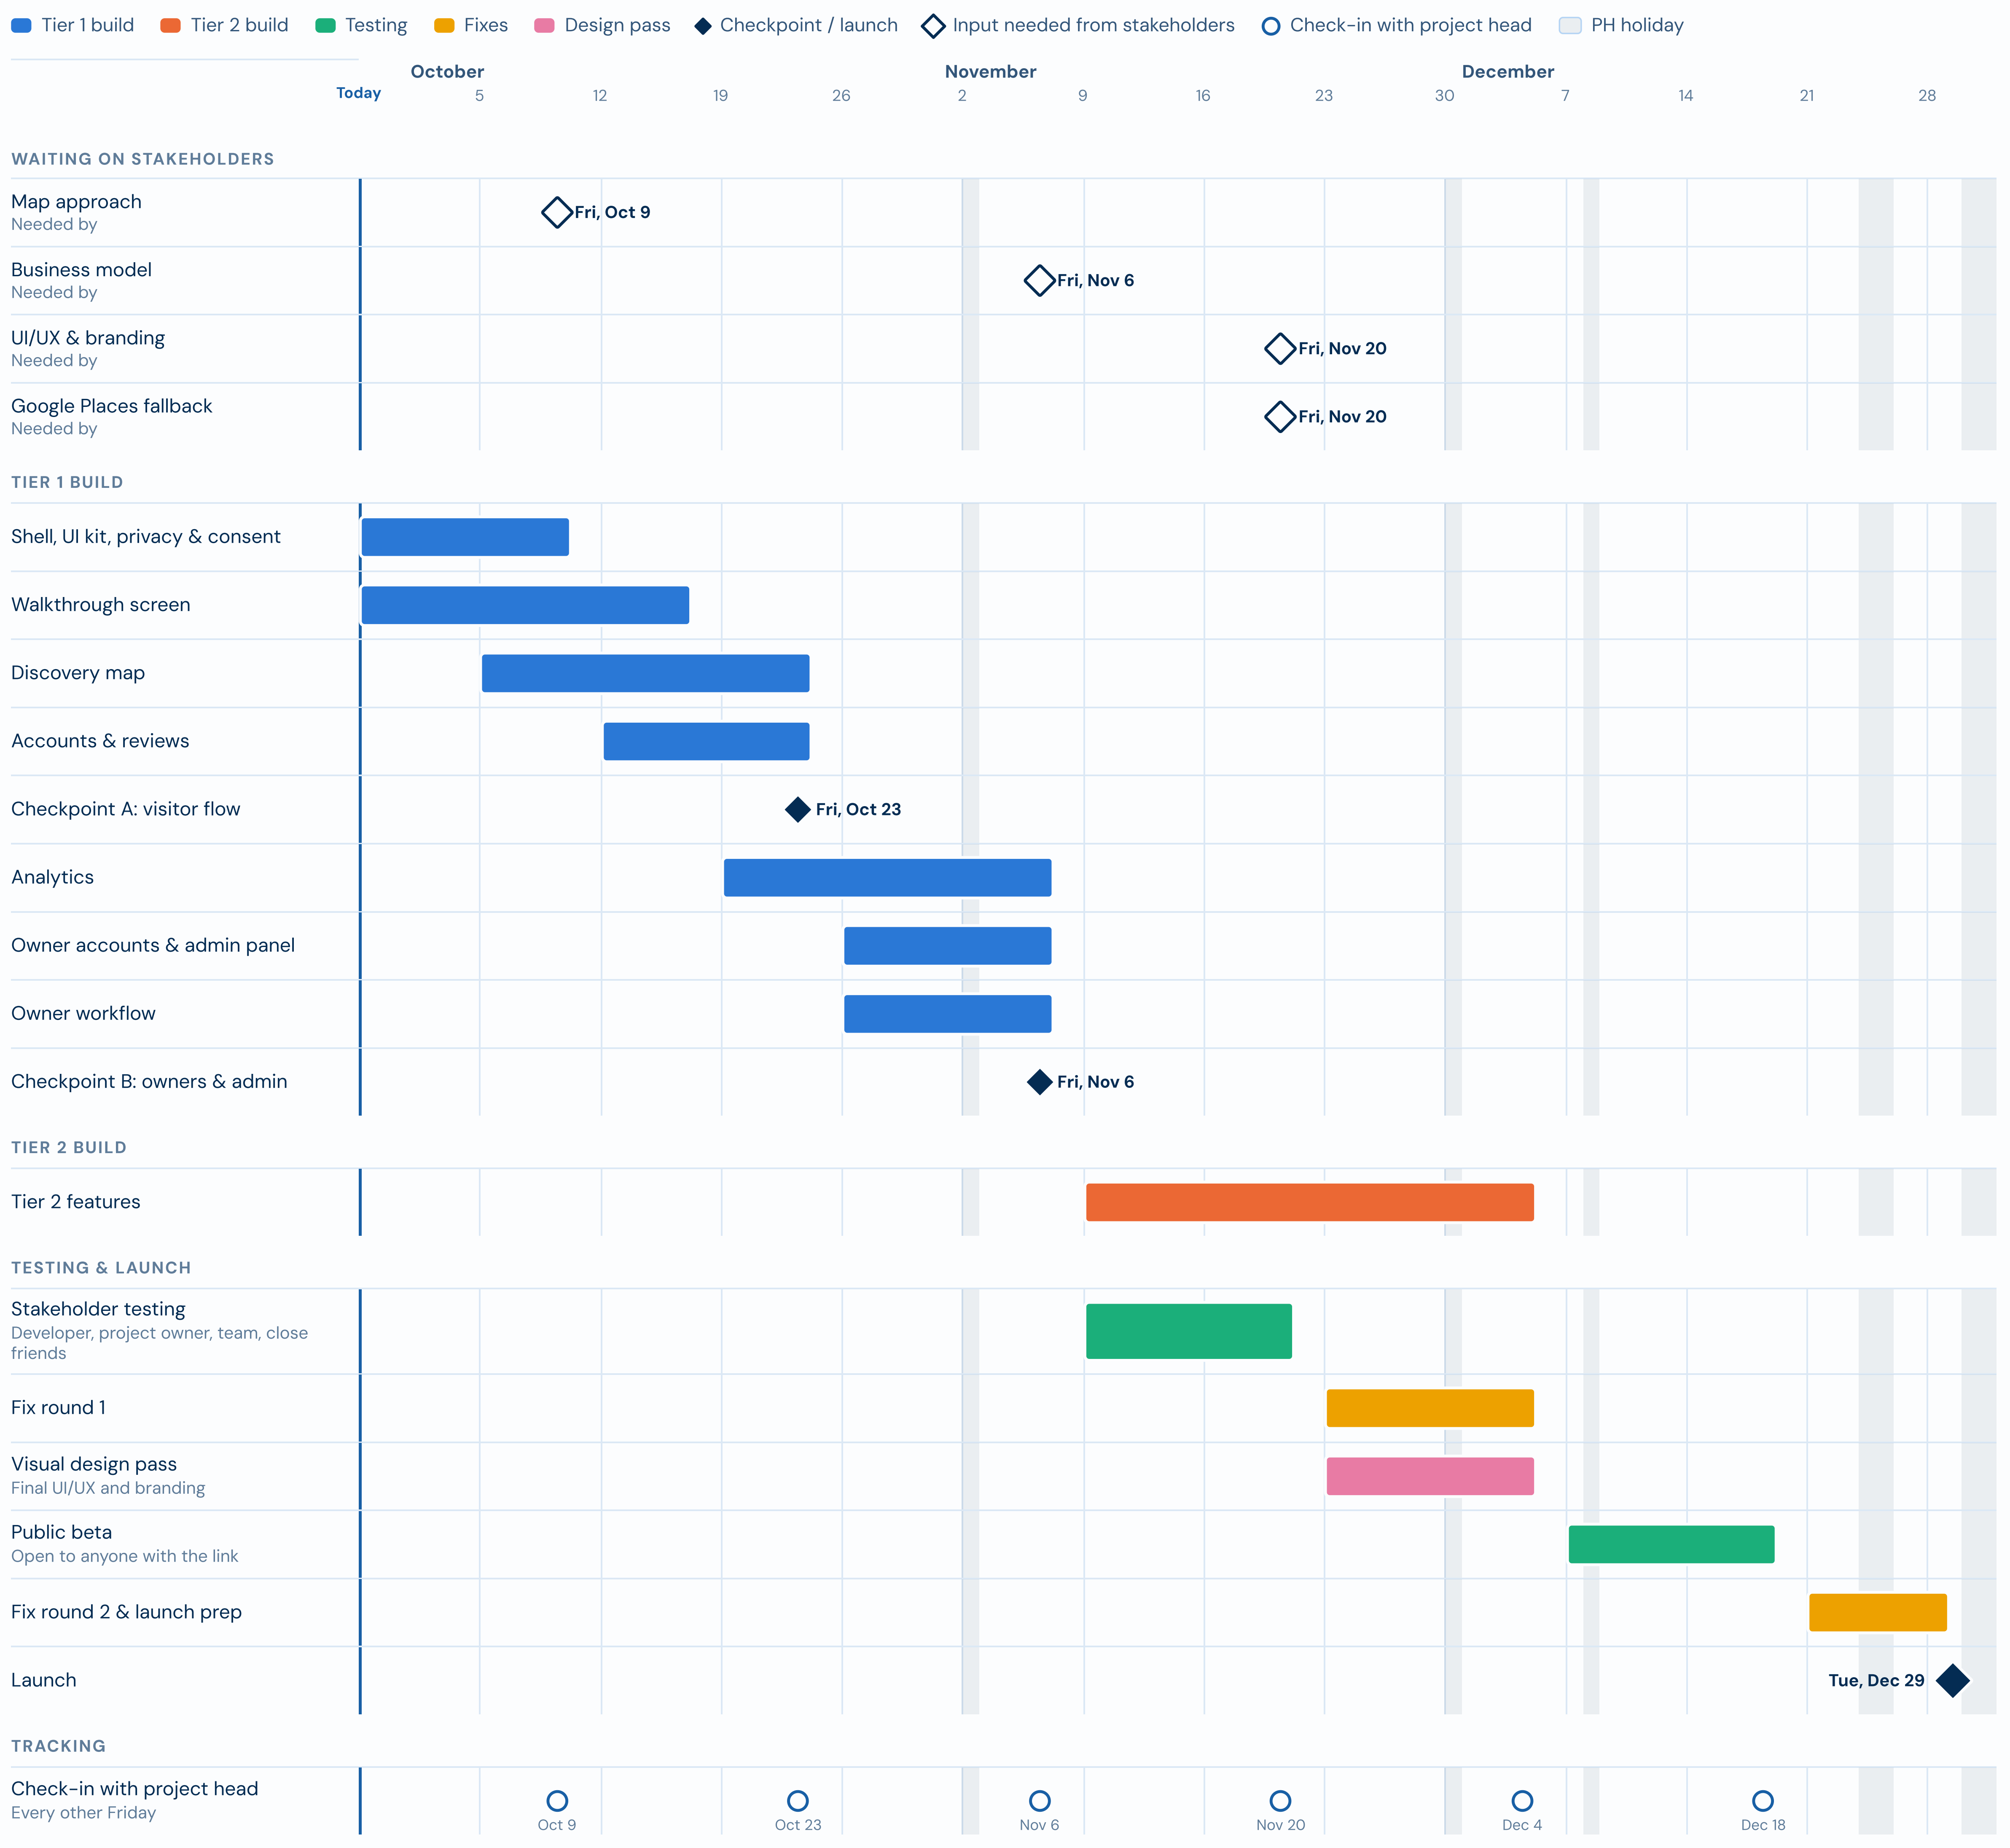

Hover or tap a bar for what's in it. Tier 3 starts after launch.

What gets built, in order

Tier 1

Before stakeholder testing · 28 Sep – 6 Nov · provisional look until the final branding arrives

VISITORS

- Map with amber (scanned) and white pins, search across Visita's own cafes, filters, Top Picks, open now, distance map approach pending
- Saved cafes, recently viewed, "I want to see inside"
- The walkthrough with its info panel, amenity cards, scan date, menu, share and deep links
- Directions hand off to Google Maps (Apple Maps option on iPhone)
- Google sign-in and reviews with rating and photo

VENUE OWNERS

- Registration with manual approval
- Listing editor, occupancy, events, review replies
- Analytics: views, walkthrough opens, directions taps, search appearances, peak hours, filters, demand

ADMIN AND LEGAL

- Venue management, scan uploads, owner approvals, amenity edit queue, review moderation
- Privacy policy, terms and storage consent (RA 10173)

Tier 2

After Tier 1, aimed at launch · 9 Nov – 4 Dec

- Amenity verification: visitors confirm or report outdated details (no points yet)
- Menu photo capture using OCR and a free-tier AI; typing the menu stays available
- Billing, handled manually: admin records payments, owners see their status waits on business model
- Marketing pages: home sections, For Cafes pricing, About, Contact, FAQ pricing waits on business model
- Offline support with a stale-data notice
- Admin demand queue
- Google Places search fallback waits on approval

Tier 3

After launch · waits on cafe-owner interviews

- Points, awards, badges, check-ins
- Referral codes, vouchers and boosted listings waits on business model
- Community page: leaderboard, most-awarded reviews
- Owner monthly report, visitor monthly recap
- Fraud monitoring, subscription and churn view, audit log

Waiting on the client or project head

Map approach Tier 1

Needed by	**Fri 9 Oct (check-in)**
What we need	Choose Google Photorealistic 3D Tiles (paid per use, about $6 per 1,000 loads after 1,000 free a month) or a pre-rendered intro video with a free map.
Blocks	The discovery map, which starts 5 Oct.
Meanwhile	Building the free option with mapcn and open map data. Switching later only changes the map layer.

Business model Tier 2

Needed by	**Fri 6 Nov (checkpoint B)**
What we need	Pricing, subscription tiers, and what a boosted listing includes.
Blocks	Manual billing, the For Cafes pricing page, and later boosted listings and vouchers.
Meanwhile	Placeholder founder pricing from the prototype: ₱2,000 onboarding and ₱150 a month.

UI/UX and branding Before beta

Needed by	**Fri 20 Nov (check-in)**
What we need	The final visual design: screens, colours, type and components.
Blocks	The visual design pass, 23 Nov – 4 Dec, before the public beta.
Meanwhile	Screens use the PRD's provisional colours and type, built on shared tokens so they can be reskinned.

Google Places search fallback Tier 2

Needed by	**Fri 20 Nov (check-in)**
What we need	Approval and a Google Cloud billing account and API key.
Blocks	Search results for cafes that aren't on Visita yet.
Meanwhile	Search covers the cafes listed on Visita. Without approval, this moves to after launch.

In-app payments After launch

Needed by	**Once the business is registered**
What we need	A payment provider for GCash and cards.
Blocks	Nothing before launch.
Meanwhile	Billing is manual: an admin records payments and owners see their status.

Points economy Tier 3

Needed by	**After launch**
What we need	What cafe owners will fund and offer: points, vouchers, boosted listings.
Blocks	Points, awards, badges, check-ins, referrals, vouchers and the leaderboard.
Meanwhile	Comes from the ongoing cafe-owner interviews.

If things slip

- **Checkpoints show slippage early.** The visitor flow is due 23 Oct and the owner and admin screens 6 Nov, both on check-in days.
- **Tier 2 gives way first.** Anything in Tier 2 not ready by 4 Dec moves to after launch, without moving the beta or launch dates.
- **Late inputs move their own work, not the launch.** If the branding arrives after 20 Nov, the beta runs on the provisional look and the design pass moves into fix round 2 or after launch. If the business model is late, billing stays manual and the pricing page shows "contact us".
- **Tier 1 is tight for one developer.** If checkpoint A slips by more than a week, we'll agree at that check-in which Tier 1 items to simplify.

Every phase

PHASE	DATES	WHAT'S IN IT
Map approach	By Fri, Oct 9	Input needed: Discovery map work starts 5 Oct. Building the free option meanwhile.
Business model	By Fri, Nov 6	Input needed: Pricing for manual billing and the For Cafes page (Tier 2).
UI/UX & branding	By Fri, Nov 20	Input needed: So the design pass lands before the public beta.
Google Places fallback	By Fri, Nov 20	Input needed: Otherwise it moves to after launch.
Shell, UI kit, privacy & consent	Mon, Sep 28 – Fri, Oct 9	Header, nav and footer; Buttons, sheets and the glass panel; Storage consent (RA 10173); Privacy and terms pages
Walkthrough screen	Mon, Sep 28 – Fri, Oct 16	Info panel: three-stat strip that expands to everything known; Menu sheet, scan date; Save and share; Directions hand-off; Deep links
Discovery map	Mon, Oct 5 – Fri, Oct 23	mapcn map with open map data; Amber and white pins; Search across Visita cafes; Filters with match count; Dock: 3D Layout, Filter, Top Picks, Saved, Recent; Pin cards and the demand button; Open now and distance
Accounts & reviews	Mon, Oct 12 – Fri, Oct 23	Google sign-in; Reviews with rating and optional photo
Checkpoint A: visitor flow	Fri, Oct 23	Review with the project head
Analytics	Mon, Oct 19 – Fri, Nov 6	Event tracking from visitor pages; Owner dashboard: views, walkthrough opens, directions taps, search appearances, peak hours, filters, demand
Owner accounts & admin panel	Mon, Oct 26 – Fri, Nov 6	Owner registration with manual approval; Venue management and scan uploads; Amenity edit queue; Review moderation
Owner workflow	Mon, Oct 26 – Fri, Nov 6	Listing editor: menu, prices, hours, events; Occupancy: quiet, moderate or full; Review replies
Checkpoint B: owners & admin	Fri, Nov 6	Review with the project head
Tier 2 features	Mon, Nov 9 – Fri, Dec 4	Amenity verification (no points); Menu photo capture (OCR + free AI); Manual billing (pricing waits on business model); Marketing pages: home, For Cafes pricing, About, Contact, FAQ; Offline support; Admin demand queue; Google Places fallback, if approved
Stakeholder testing	Mon, Nov 9 – Fri, Nov 20	Developer, project owner, team members and close friends; Tests the flows on the provisional look; Collect issues for fix round 1
Fix round 1	Mon, Nov 23 – Fri, Dec 4	Fixes from stakeholder testing; Tier 2 continues alongside
Visual design pass	Mon, Nov 23 – Fri, Dec 4	Apply the final UI/UX and branding to every screen; Screens are built on shared tokens and components, so this is a reskin rather than a rebuild; Public beta ships with the final look
Public beta	Mon, Dec 7 – Fri, Dec 18	Open to anyone with the link; Collect issues for fix round 2
Fix round 2 & launch prep	Mon, Dec 21 – Mon, Dec 28	Fixes from the beta; Production domain, data and monitoring
Launch	Tue, Dec 29	Public launch
Check-ins with project head	Oct 9, Oct 23, Nov 6, Nov 20, Dec 4, Dec 18	Bi-weekly progress review, Fridays
PH holidays	Nov 2, Nov 30, Dec 8, Dec 24–25, Dec 30–31	All Souls' Day; Bonifacio Day; Immaculate Conception; Christmas Eve and Day; Rizal Day and New Year's Eve
